Gantt [Critical-Waterfall]

Print Date: 25-Jul-23
Data Date: 24-Jul-23

Activity ID	Activity Name	Owner	Original Duration	Remaining Duration	Physical % Complete	Early Start (A=Actual)	Early Finish (A=Actual)	Late Start	Late Finish	Total Float
Puma Prime SP: 3604-80			441	382		19-Jun-23 A	03-Feb-25	25-Jul-23	03-Feb-25	0
CRU3000	Acquire Archeology Consultant	Kurt2And	45	0	100%	19-Jun-23 A	05-Jul-23 A	22-Aug-23	22-Aug-23	
CRU3005	Conduct Archeology Desktop Review	Kurt2And	45	0	100%	06-Jul-23 A	07-Jul-23 A	22-Aug-23	22-Aug-23	
PMM2000	Conduct Project Kick-Off Meeting	Bitt1Jam	1	0	100%	24-Jul-23 A	24-Jul-23 A	25-Jul-23	25-Jul-23	
WTL1010	Delineate Wetlands (Level 1)	Lee1Tho	5	5	0%	25-Jul-23	31-Jul-23	06-Jun-24	12-Jun-24	218
TRF1000	Prepare Traffic Forecasts and ESALs	Olso1Kri	5	5	0%	25-Jul-23	31-Jul-23	27-Oct-23	02-Nov-23	67
EDD1000	Prepare & Submit EDD 1	Fulm1Zac	5	5	0%	25-Jul-23	31-Jul-23	30-Oct-24	05-Nov-24	319
ENM1000	Prepare & Distribute ENM	Carn1Sta	10	10	0%	25-Jul-23	07-Aug-23	01-Aug-23	14-Aug-23	5
SDL1020	Conduct As-Built Alignment Surveys	Mist1Dre	10	10	0%	25-Jul-23	07-Aug-23	20-Oct-23	02-Nov-23	62
CRU1000	Received ENM	Kurt2And	0	0	0%	08-Aug-23		15-Aug-23		5
WTL1020	Delineate Wetlands (Level 2)	Lee1Tho	10	10	0%	01-Aug-23	14-Aug-23	13-Jun-24	26-Jun-24	73
CRU1020	Conduct Preliminary CRU Evaluation	Kurt2And	5	5	0%	08-Aug-23	14-Aug-23	15-Aug-23	21-Aug-23	5
NOI1000	Determine Level of Noise Analysis	Bitt1Jam	5	5	0%	08-Aug-23	14-Aug-23	08-Nov-23	15-Nov-23	65
4FD1000	Prepare Draft De Minimis Section 4(f) Impact Request Form	Carn1Sta	5	5	0%	08-Aug-23	14-Aug-23	09-Apr-24	15-Apr-24	167
PWP1000	Coordinate Permitting Needs With DNR	mill1rac	10	10	0%	08-Aug-23	21-Aug-23	13-Dec-23	27-Dec-23	87
PSR1000	Review Protected Species by OES	Smit2Chr	10	10	0%	08-Aug-23	21-Aug-23	05-Jun-24	18-Jun-24	207
DME1000	Prepare Preliminary Design Memo in District	Bitt1Jam	20	20	0%	25-Jul-23	21-Aug-23	01-Aug-23	28-Aug-23	5
CRU3007	Obtain Right of Access [District]	Arnd1Mar	5	5	0%	15-Aug-23	21-Aug-23	22-Aug-23	28-Aug-23	5
4FD1010	Review Draft De Minimis Section 4(f) Impact Request Form by OES	Elli1Lis	5	5	0%	15-Aug-23	21-Aug-23	16-Apr-24	22-Apr-24	167
EDD1010	Review & Respond to EDD 1	Olso1Gra	20	20	0%	01-Aug-23	28-Aug-23	06-Nov-24	06-Dec-24	319
SDE1010	Conduct Topography/DTM Survey	Mist1Dre	25	25	0%	25-Jul-23	28-Aug-23	25-Jul-23	28-Aug-23	0
SDE1020	Conduct Drainage Survey	Mist1Dre	25	25	0%	25-Jul-23	28-Aug-23	25-Jul-23	28-Aug-23	0
SDE1030	Conduct Utilities Survey	Mist1Dre	25	25	0%	25-Jul-23	28-Aug-23	25-Jul-23	28-Aug-23	0
SDE1000	Annotate/Fill Voids on Photo Map/Topography/DTM Survey	Mist1Dre	25	25	0%	25-Jul-23	28-Aug-23	25-Jul-23	28-Aug-23	0
4FD1020	Revise Draft De Minimis Section 4(f) Impact Request Form to Incorp	Carn1Sta	5	5	0%	22-Aug-23	28-Aug-23	23-Apr-24	29-Apr-24	167
WTL1030	Prepare Wetlands Report	Lee1Tho	15	15	0%	15-Aug-23	05-Sep-23	27-Jun-24	18-Jul-24	217
TMP1000	Prepare TMP	Bitt1Jam	5	5	0%	29-Aug-23	05-Sep-23	20-Jun-24	26-Jun-24	202
TMP0900	Determine Construction Staging	Bitt1Jam	30	30	0%	25-Jul-23	05-Sep-23	03-Nov-23	19-Dec-23	72
SDL1000	Conduct Public Land Surveys (PLS)	Stra1Tod	30	30	0%	25-Jul-23	05-Sep-23	26-Jul-24	06-Sep-24	252
SDL1030	Conduct Existing Properties Surveys	Mist1Dre	30	30	0%	25-Jul-23	05-Sep-23	26-Jul-24	06-Sep-24	252
TMP1010	Review Draft TMP by Traffic	Rogn1Mic	5	5	0%	06-Sep-23	12-Sep-23	27-Jun-24	03-Jul-24	202
ENM1020	Review & Respond to ENM by CMMT	Olso1Gra	30	30	0%	08-Aug-23	19-Sep-23	05-Jun-24	18-Jul-24	207
ENM1030	Review & Respond to ENM by Regulated Materials	Alle1Sum	30	30	0%	08-Aug-23	19-Sep-23	05-Jun-24	18-Jul-24	207
FPA1000	Prepare Floodplain Assessment	mill1rac	30	30	0%	08-Aug-23	19-Sep-23	05-Jun-24	18-Jul-24	207
PSR1010	Review Protected Species by U.S. Fish and Wildlife	Smit2Chr	20	20	0%	22-Aug-23	19-Sep-23	20-Jun-24	18-Jul-24	207
SDL1010	Conduct Existing Right of Way Surveys	Mist1Dre	30	30	0%	08-Aug-23	19-Sep-23	03-Nov-23	19-Dec-23	62
MDR1000	Conduct Roadway Borings/Field Work	Olso1Kri	20	20	0%	29-Aug-23	26-Sep-23	06-Oct-23	02-Nov-23	27
4FD1030	Review Draft De Minimis Section 4(f) Impact Request Form by FHW	Elli1Lis	30	30	0%	29-Aug-23	27-Sep-23	30-Apr-24	29-May-24	245
CRU1030	Conduct Tribal, MIAC, and OSA Consultation	Kurt2And	45	45	0%	15-Aug-23	28-Sep-23	11-Mar-24	24-Apr-24	209
4FD1040	Prepare Public Notice (Only for Catex Documents)	Carn1Sta	5	5	0%	28-Sep-23	04-Oct-23	15-Jul-24	19-Jul-24	197
MDR1005	Prepare Preliminary MDR	Olso1Kri	10	10	0%	27-Sep-23	10-Oct-23	03-Nov-23	17-Nov-23	27
MDR1010	Prepare Pavement Alternatives/PDM/LCCA	Olso1Kri	10	10	0%	27-Sep-23	10-Oct-23	03-Nov-23	17-Nov-23	27
EMP1000	Prepare Preliminary Environmental Management Plan	Carn1Sta	15	15	0%	20-Sep-23	10-Oct-23	19-Jul-24	08-Aug-24	207
LAY1040	Prepare Preliminary Geometric Layout & Profile	Holc1Abi	30	30	0%	29-Aug-23	10-Oct-23	29-Aug-23	10-Oct-23	0
4FD1050	Public Notice of Intent for a De Minimis Section 4(f) Impact Finding	Carn1Sta	14	14	0%	28-Sep-23	11-Oct-23	30-May-24	12-Jun-24	245
LAY1043	Submit Preliminary Geometric Layout & Profile to GDSU	Holc1Abi	2	2	0%	11-Oct-23	12-Oct-23	11-Oct-23	12-Oct-23	0
4FD1060	Prepare De Minimis Section 4(f) Concurrence letter for the Official w	Carn1Sta	5	5	0%	12-Oct-23	18-Oct-23	13-Jun-24	20-Jun-24	167
4FD1070	Review De Minimis Section 4(f) Concurrence Letter for the Official w	Elli1Lis	5	5	0%	19-Oct-23	25-Oct-23	21-Jun-24	27-Jun-24	167
EMP2000	Prepare Final Environmental Management Plan	Carn1Sta	15	15	0%	11-Oct-23	31-Oct-23	09-Aug-24	29-Aug-24	207
DME1010	Conduct GDSU Review of Preliminary Design Memo	Schl3Mat	15	15	0%	11-Oct-23	31-Oct-23	13-Oct-23	02-Nov-23	2
4FD1080	Revise De Minimis Section 4(f) Concurrence Letter for the Official wi	Carn1Sta	5	5	0%	26-Oct-23	01-Nov-23	28-Jun-24	05-Jul-24	167
LAY1045	Conduct GDSU Review of Preliminary Layout (Optional for Level 2	Schl3Mat	15	15	0%	13-Oct-23	02-Nov-23	13-Oct-23	02-Nov-23	0
MDR1030	Review of LCCA by Maplewood/Industy	Olso1Kri	20	20	0%	11-Oct-23	07-Nov-23	20-Nov-23	19-Dec-23	27
CRU3010	Conduct Archeology Field Investigation	Kurt2And	60	60	0%	15-Aug-23	07-Nov-23	22-Aug-23	15-Nov-23	5
NOI1010	Procure Prequalified Noise Consultant	Bitt1Jam	60	60	0%	15-Aug-23	07-Nov-23	16-Nov-23	14-Feb-24	65
NOI1020	Develop Receptor Sites	Bitt1Jam	5	5	0%	08-Nov-23	15-Nov-23	15-Feb-24	22-Feb-24	65
4FD1090	Obtain Official Jurisdiction letter signature by FHWA	Elli1Lis	10	10	0%	02-Nov-23	16-Nov-23	08-Jul-24	19-Jul-24	167
EGL1000	Conduct Eagle Survey	Smit2Chr	5	5	0%	15-Nov-23	21-Nov-23	26-Mar-24	01-Apr-24	88
NOI1015	Prepare and Hold Initial Public Noise Meeting (if needed)	Bitt1Jam	10	10	0%	08-Nov-23	22-Nov-23	01-Mar-24	14-Mar-24	75
NOI1025	Approve Receptor Sites	Bitt1Jam	5	5	0%	16-Nov-23	22-Nov-23	23-Feb-24	29-Feb-24	65
MS_180	MDR Completed	Bitt1Jam	0	0	0%		01-Dec-23		01-Aug-24	167
MDR1060	Prepare Final MDR	Olso1Kri	15	15	0%	08-Nov-23	01-Dec-23	30-Apr-24	20-May-24	117
CRU3020	Conduct Archeology Field Investigation Review	Kurt2And	15	15	0%	08-Nov-23	01-Dec-23	22-Nov-23	14-Dec-23	9
NOI1030	Monitor Noise	Bitt1Jam	10	10	0%	27-Nov-23	08-Dec-23	01-Mar-24	14-Mar-24	65
4FD1100	FHWA Issues Final De Minimis Section 4(f) Finding	Elli1Lis	14	14	0%	17-Nov-23	08-Dec-23	22-Jul-24	08-Aug-24	167
LAY1050	Prepare Final Geometric Layout & Profile	Holc1Abi	30	30	0%	03-Nov-23	19-Dec-23	03-Nov-23	19-Dec-23	0
LAY1053	Submit Final Geometric Layout & Profile to GDSU	Holc1Abi	2	2	0%	20-Dec-23	21-Dec-23	15-Mar-24	18-Mar-24	58
LAY1060	Conduct GDSU Review of Final Geometric Layout & Profile (Optior	Schl3Mat	10	10	0%	22-Dec-23	08-Jan-24	19-Mar-24	01-Apr-24	58
NOI1040	Model Noise Impact for All Alternatives	Bitt1Jam	22	22	0%	11-Dec-23	11-Jan-24	15-Mar-24	15-Apr-24	65
LIM1000	Build Preliminary Model	Vona1Tod	20	20	0%	20-Dec-23	19-Jan-24	20-Dec-23	19-Jan-24	0
NOI1055	Prepare and Hold Public Noise Meeting	Bitt1Jam	10	10	0%	12-Jan-24	26-Jan-24	14-May-24	28-May-24	85
LIM1004	Construction Impacts Review	Bitt1Jam	5	5	0%	22-Jan-24	26-Jan-24	22-Jan-24	26-Jan-24	0
DME1020	Revise and Sign Design Memo by District	Bitt1Jam	20	20	0%	09-Jan-24	06-Feb-24	02-Apr-24	29-Apr-24	58
LAY1075	Revise and Sign Geometric Layout by District	Holc1Abi	20	20	0%	09-Jan-24	06-Feb-24	02-Apr-24	29-Apr-24	58
MS_185	Layout Approved	Bitt1Jam	0	0	0%		13-Feb-24		20-May-24	68
DME1030	Approval of Formal Design Exception by State Design Engineer	Schl3Mat	5	5	0%	07-Feb-24	13-Feb-24	30-Apr-24	06-May-24	58
LAY1080	State Design Engineer Approve Geometric Layout (Level 1 Only)	Schl3Mat	5	5	0%	07-Feb-24	13-Feb-24	30-Apr-24	06-May-24	58
HYD1000	Prepare Preliminary Hydraulics Design	kord1ada	40	40	0%	20-Dec-23	16-Feb-24	28-Dec-23	26-Feb-24	5
NOI1050	Model Noise Mitigation for Preferred Alternative	Bitt1Jam	30	30	0%	12-Jan-24	26-Feb-24	16-Apr-24	28-May-24	65
LIM1005	Prepare Title Limits	Vona1Tod	20	20	0%	29-Jan-24	26-Feb-24	29-Jan-24	26-Feb-24	0
RTT0085	Prepare Title Map [District]	Fulm1Zac	1	1	0%	27-Feb-24	27-Feb-24	12-Aug-24	12-Aug-24	116
RTT1020	Determine Unrecorded Utilities Easements [District]	Fulm1Zac	5	5	0%	28-Feb-24	05-Mar-24	16-Sep-24	20-Sep-24	139
RTT0090	Acquire Consultant for Title Opinions [OLM]	Bult1Con	8	8	0%	28-Feb-24	08-Mar-24	13-Aug-24	22-Aug-24	116
NOI1060	Draft Noise Report	Bitt1Jam	10	10	0%	27-Feb-24	11-Mar-24	29-May-24	11-Jun-24	65
RTT0095	Prepare Title Opinions [OLM]	Bult1Con	10	10	0%	11-Mar-24	22-Mar-24	23-Aug-24	06-Sep-24	116
NOI1065	Prepare and Hold Follow Up Public Noise Meeting (if needed)	Bitt1Jam	10	10	0%	12-Mar-24	25-Mar-24	26-Jul-24	08-Aug-24	95
NOI1070	Review Draft Noise Report [District]	Bitt1Jam	10	10	0%	12-Mar-24	25-Mar-24	12-Jun-24	26-Jun-24	65
CRU3030	Conduct Archeology Evaluation	Kurt2And	80	80	0%	04-Dec-23	28-Mar-24	15-Dec-23	10-Apr-24	9
RTT1010	Confirm Title Opinions Complete [District]	Mist1Abb	7	7	0%	25-Mar-24	02-Apr-24	12-Sep-24	20-Sep-24	119
CRU3040	Conduct Archeology Evaluation Review	Kurt2And	10	10	0%	29-Mar-24	11-Apr-24	11-Apr-24	24-Apr-24	9
NOI1075	Review Draft Noise Report [EMTU]	Rose1Mel	15	15	0%	26-Mar-24	15-Apr-24	27-Jun-24	18-Jul-24	65
NOI1080	Incorporate Comments & Prepare Final Noise Report	Bitt1Jam	15	15	0%	16-Apr-24	06-May-24	19-Jul-24	08-Aug-24	65
LIM1010	Review & Revise Model	Vona1Tod	50	50	0%	27-Feb-24	06-May-24	27-Feb-24	06-May-24	0
CRU1300	Prepare & Distribute CRU Findings Letter	Kurt2And	20	20	0%	12-Apr-24	09-May-24	25-Apr-24	22-May-24	9
PLN3000	Prepare 30% Plans	Bitt1Jam	10	10	0%	07-May-24	20-May-24	07-May-24	20-May-24	0
ADR1000	Prepare Detour Agreement	Hadr1Lau	5	5	0%	21-May-24	28-May-24	27-Jan-25	03-Feb-25	170
PLN3250	Complete Streets 30% Review	Bitt1Jam	10	10	0%	21-May-24	04-Jun-24	05-Jul-24	18-Jul-24	30
PLN3500	Conduct 30% Plan Review	Bitt1Jam	10	10	0%	21-May-24	04-Jun-24	20-Jun-24	03-Jul-24	20
HYD1030	Prepare Preliminary SWPPP and Erosion Control Plans	kord1ada	15	15	0%	21-May-24	11-Jun-24	27-Jun-24	18-Jul-24	25
CRU1320	Obtain SHPO Concurrence (When Applicable)	Kurt2And	35	35	0%	10-May-24	13-Jun-24	23-May-24	26-Jun-24	13
TCP1000	Prepare Traffic Control Plan	Hadr1Lau	20	20	0%	21-May-24	18-Jun-24	05-Jul-24	01-Aug-24	30
NOI1090	Solicit Benefited Receptors & Document Results of Noise Solicitatio	Bitt1Jam	30	30	0%	07-May-24	18-Jun-24	09-Aug-24	20-Sep-24	65
LIM1020	Prepare & Submit Construction Limits	Vona1Tod	10	10	0%	05-Jun-24	18-Jun-24	05-Jul-24	18-Jul-24	20
LIM1030	Review and Approve Final Construction Limits	Bitt1Jam	0	0	0%		18-Jun-24		18-Jul-24	20
UTI1000	Send Plan Information & Conduct Utility Information Meetings	Bitt1Jam	15	15	0%	05-Jun-24	26-Jun-24	08-Jul-24	26-Jul-24	21
SGN1000	Prepare Signing Plan	Hadr1Lau	15	15	0%	05-Jun-24	26-Jun-24	30-Sep-24	18-Oct-24	80
TMP1020	Finalize TMP	Bitt1Jam	5	5	0%	20-Jun-24	26-Jun-24	23-Aug-24	29-Aug-24	45
EDD2000	Prepare & Submit EDD 2	Fulm1Zac	5	5	0%	20-Jun-24	26-Jun-24	09-Dec-24	13-Dec-24	117
SGN1010	Prepare Signing Special Provisions	Hadr1Lau	3	3	0%	27-Jun-24	01-Jul-24	23-Oct-24	25-Oct-24	82
HYD1010	Prepare Final Hydraulics Design	kord1ada	30	30	0%	21-May-24	03-Jul-24	05-Jun-24	18-Jul-24	10
EDD2010	Review & Respond to EDD 2	Olso1Gra	5	5	0%	27-Jun-24	03-Jul-24	16-Dec-24	20-Dec-24	117
WTL2000	Prepare Wetland 2 Part Finding	Lee1Tho	15	15	0%	20-Jun-24	11-Jul-24	19-Jul-24	08-Aug-24	20
PLN6000	Prepare 60% Plans	Bitt1Jam	40	40	0%	21-May-24	18-Jul-24	21-May-24	18-Jul-24	0
TPM1000	Prepare Pavement Marking Plan	Hadr1Lau	10	10	0%	19-Jul-24	01-Aug-24	19-Jul-24	01-Aug-24	0
PLN6500	Conduct 60% Plan Review	Bitt1Jam	10	10	0%	19-Jul-24	01-Aug-24	16-Aug-24	29-Aug-24	20
PWP1010	Prepare & Submit DNR Public Waters Permit Application	mill1rac	15	15	0%	19-Jul-24	08-Aug-24	20-Aug-24	10-Sep-24	22
WTP1010	Prepare & Submit Combined Permit Application	Lee1Tho	20	20	0%	12-Jul-24	08-Aug-24	10-Sep-24	08-Oct-24	42
MS_245	Army Corps Permit Application Submitted	Bitt1Jam	0	0	0%		08-Aug-24		04-Dec-24	80
UTI1010	Conduct Utility Design Meeting	Bitt1Jam	15	15	0%	19-Jul-24	08-Aug-24	29-Jul-24	16-Aug-24	6
HYD1040	Prepare Final SWPPP and Erosion Control Plans	kord1ada	15	15	0%	19-Jul-24	08-Aug-24	09-Aug-24	29-Aug-24	15
WTP1040	Permit Application Complete	Lee1Tho	0	0	0%		29-Aug-24		29-Oct-24	42
WTP1030	Respond to COE Draft Permit Questions	Lee1Tho	15	15	0%	09-Aug-24	29-Aug-24	08-Oct-24	29-Oct-24	42
PLN9000	Prepare 90% Plans	Bitt1Jam	20	20	0%	02-Aug-24	29-Aug-24	02-Aug-24	29-Aug-24	0
NPP1040	Prepare NPDES Permit Application		5	5	0%	30-Aug-24	06-Sep-24	21-Oct-24	25-Oct-24	35
CTX1000-01	Prepare CATEX Document	Carn1Sta	30	30	0%	30-Jul-24	10-Sep-24	09-Aug-24	20-Sep-24	8
MS_150	Environmental Document Approved	Bitt1Jam	0	0	0%		10-Sep-24		25-Oct-24	33
RWP1000	Prepare Authorization & Work Maps [District]	Fulm1Zac	10	10	0%	27-Aug-24	10-Sep-24	09-Sep-24	20-Sep-24	8
CRU1370	Prepare Agreement (Memorandum) Use for Adverse Effect Only	Kurt2And	60	60	0%	14-Jun-24	10-Sep-24	27-Jun-24	20-Sep-24	8
TUR1020	Conduct QMP Check by District	Bitt1Jam	10	10	0%	30-Aug-24	13-Sep-24	07-Oct-24	18-Oct-24	25
RWP1025	Prepare Certification of Location (COLGCs) [District]	Stra1Tod	4	4	0%	11-Sep-24	16-Sep-24	04-Oct-24	09-Oct-24	17
UTI1020	Obtain & Review Utility Relocation Plans, Schedules & Estimate & F	Bitt1Jam	30	30	0%	09-Aug-24	20-Sep-24	19-Aug-24	30-Sep-24	6
RWP1020	Prepare Plats [District]	Mist1Abb	8	8	0%	11-Sep-24	20-Sep-24	30-Sep-24	09-Oct-24	13
PWP1020	Public Waters Review by DNR	mill1rac	45	45	0%	09-Aug-24	22-Sep-24	11-Sep-24	25-Oct-24	33
PWP1030	DNR Public Waters Permit Received	mill1rac	0	0	0%		23-Sep-24		25-Oct-24	25
UTI1030	Prepare & Send Utility Verification Letters	Bitt1Jam	2	2	0%	23-Sep-24	24-Sep-24	01-Oct-24	02-Oct-24	6
RWP1080	Prepare Right of Way Packages [District]	Arnd1Mar	13	13	0%	11-Sep-24	27-Sep-24	23-Sep-24	09-Oct-24	8
PRO1020	Receive Special Provisions from City	Pirk1Wil	0	0	0%		27-Sep-24		18-Oct-24	15
PLN9010	Conduct 90% Plan Review	Bitt1Jam	20	20	0%	30-Aug-24	27-Sep-24	30-Aug-24	27-Sep-24	0
RPR1000	Receive and Distribute Right of Way Package [OLM]	Moen1Sco	2	2	0%	30-Sep-24	01-Oct-24	10-Oct-24	11-Oct-24	8
RPR1020	Review and Approve Plat Descriptions [OLM]	Roro1Fuf	5	5	0%	02-Oct-24	08-Oct-24	04-Nov-24	08-Nov-24	23
RPR1070	Prepare Attorney's Condition of Title [OLM]	Bult1Con	5	5	0%	02-Oct-24	08-Oct-24	04-Nov-24	08-Nov-24	23
AUT1030	Write Agreement	Bojo1Mar	15	15	0%	23-Sep-24	11-Oct-24	18-Oct-24	08-Nov-24	20
AUT1040	Send Agreement to Utility Owner for Signature	Bojo1Mar	1	1	0%	14-Oct-24	14-Oct-24	08-Nov-24	12-Nov-24	20
PLN9500	Prepare 95% Plan	Bitt1Jam	15	15	0%	30-Sep-24	18-Oct-24	30-Sep-24	18-Oct-24	0
UTI1040	Verification Letter Responses	Bitt1Jam	22	22	0%	25-Sep-24	24-Oct-24	03-Oct-24	01-Nov-24	6
WTP1070	Prepare WCA Notification	Brow1Eli	40	40	0%	30-Aug-24	25-Oct-24	04-Dec-24	03-Feb-25	65
UTI1070	Prepare & Send Utility Notice & Orders	Bojo1Mar	1	1	0%	25-Oct-24	25-Oct-24	31-Jan-25	03-Feb-25	65
TUR1030	Prepare Final Construction Cost Estimate by District	Bitt1Jam	5	5	0%	21-Oct-24	25-Oct-24	21-Oct-24	25-Oct-24	0
PRO1000	Prepare Special Provisions	Pirk1Wil	15	15	0%	07-Oct-24	25-Oct-24	07-Oct-24	25-Oct-24	0
TTT1000	Prepare Time and Traffic	Pirk1Wil	5	5	0%	21-Oct-24	25-Oct-24	21-Oct-24	25-Oct-24	0
RPR1040	Review and Approve Plats [OLM]	Bong1Jas	20	20	0%	02-Oct-24	29-Oct-24	14-Oct-24	08-Nov-24	8
RPR1030	Write Narrative Description [OLM]	Roro1Fuf	20	20	0%	02-Oct-24	29-Oct-24	18-Oct-24	15-Nov-24	12
MS_230	Project Turned In	Bitt1Jam	0	0	0%		01-Nov-24		01-Nov-24	0

Remaining Level of Effort
Actual Work
Actual Level of Effort
Remaining ...

TASK filter: All Activities

Gantt [Critical-Waterfall]

Print Date: 25-Jul-23
Data Date: 24-Jul-23

Activity ID	Activity Name	Owner	Original Duration	Remaining Duration	Physical % Complete	Early Start (A=Actual)	Early Finish (A=Actual)	Late Start	Late Finish	Total Float
TUR1040	Prepare Submittal Memo and Submit Plans & Specs	BillLiam	5	5	0%	28-Oct24	01-Nov24	28-Oct24	01-Nov24	0
RPR1050	Perform Plotting Monumentation [District]	MattAlab	5	5	0%	30-Oct24	05-Nov24	12-Nov24	18-Nov24	8
RVL1010	Complete Valuations/Minimum Comp [OLM]	CoreWar	20	20	0%	11-Oct24	07-Nov24	23-Oct24	20-Nov24	8
RPR1060	File Plats [District]	DickLoos	2	2	0%	06-Nov24	07-Nov24	19-Nov24	20-Nov24	8
AUT1030	Receive Signed Agreement from Utility Owner	BojorMar	20	20	0%	15-Oct24	12-Nov24	12-Nov24	12-Dec24	20
RPR1080	Prepare Conveyance Documents [OLM]	BuffCon	10	10	0%	30-Oct24	13-Nov24	18-Nov24	03-Dec24	12
RVL1020	Review & Certify Valuations [OLM]	CoreWar	4	4	0%	08-Nov24	14-Nov24	21-Nov24	26-Nov24	8
RPR1090	Prepare Commissioner's Orders [OLM]	HendTrav	5	5	0%	08-Nov24	15-Nov24	25-Nov24	03-Dec24	10
CPM2000	Project Contingency/Buffer	BillLiam	10	10	0%	04-Nov24	18-Nov24	04-Nov24	18-Nov24	0
RPR1100	Encumber Funds [OLM]	MeanSco	3	3	0%	15-Nov24	19-Nov24	27-Nov24	03-Dec24	8
RPR1110	Prepare Direct Purchase Packages [OLM]	JohnFarb	3	3	0%	20-Nov24	22-Nov24	04-Dec24	06-Dec24	8
ADMI1005-B	Acceptance of District Turn In Package	ReamNan	5	5	0%	19-Nov24	25-Nov24	19-Nov24	25-Nov24	0
WTP1080	Process 404 Permit (Specify GP, LOP, SIP) COE Review	LeeThe	90	90	0%	30-Aug-24	27-Nov24	29-Oct24	27-Jan25	61
WTP1050	Process 401 MPCA Review	LeeThe	90	90	0%	30-Aug-24	27-Nov24	29-Oct24	27-Jan25	61
AUT1060	Execute Agreement	BojorMar	15	15	0%	13-Nov24	05-Dec24	12-Dec24	06-Jan25	20
WTP1080	MnDOT Receives & signs 401/404 Section 10	LeeThe	5	5	0%	02-Dec24	06-Dec24	27-Jan25	03-Feb25	38
RDP1000	Make Direct Purchase Offer [District]	AndrMar	10	10	0%	25-Nov24	10-Dec24	09-Dec24	20-Dec24	8
TUR1050	Incorporate CO Plans, Specs, & Estimate Revisions	BillLiam	10	10	0%	26-Nov24	11-Dec24	19-Dec24	06-Jan25	16
RDP1030	Complete Purchase-Sign Document Files [District]	AndrMar	2	2	0%	11-Dec24	12-Dec24	06-Jan25	10-Jan25	19
RDP1010	30-Day Minimum Consideration Period [District]	AndrMar	8	8	0%	11-Dec24	19-Dec24	22-Dec24	30-Dec24	12
RDP1005	Negotiate Direct Purchase Offer [District]	AndrMar	16	16	0%	25-Nov24	18-Dec24	09-Dec24	30-Dec24	7
ADMI1030-B	Post Turn In Activities	ReamNan	20	20	0%	26-Nov24	26-Dec24	26-Nov24	26-Dec24	0
RDP1050	Prepare Closing Package [OLM]	JohnFarb	10	10	0%	13-Dec24	27-Dec24	10-Jan25	27-Jan25	19
ADMI1045-B	FHWA Authorization	ReamNan	7	7	0%	27-Dec24	03-Jan25	27-Dec24	03-Jan25	0
ADMI1045-B	Create Proposal Ad	ReamNan	2	2	0%	02-Jan-25	06-Jan25	02-Jan25	06-Jan25	0
RDP1060	Make Direct Purchase Final Payment [OLM]	JohnFarb	5	5	0%	30-Dec24	06-Jan25	27-Jan25	03-Feb25	19
ME_250	RW Title and Possession Obtained [District]	DickLoos	0	0	0%		22-Jan25		03-Feb25	8
RED1020	Hearing on Petition to Title & Possession [OLM]	BuffCon	35	35	0%	19-Dec24	22-Jan25	30-Dec24	03-Feb25	12
CPM1000	Perform Ongoing Project Management	BillLiam	441	382	0%	24-Jul-23 A	03-Feb25	25-Jul-23	03-Feb25	0
ME_270	Letting Held	BillLiam	0	0	0%		03-Feb25		03-Feb25	0
ADMI1050-B	Advertise	ReamNan	20	20	0%	06-Jan25	03-Feb25	06-Jan25	03-Feb25	0

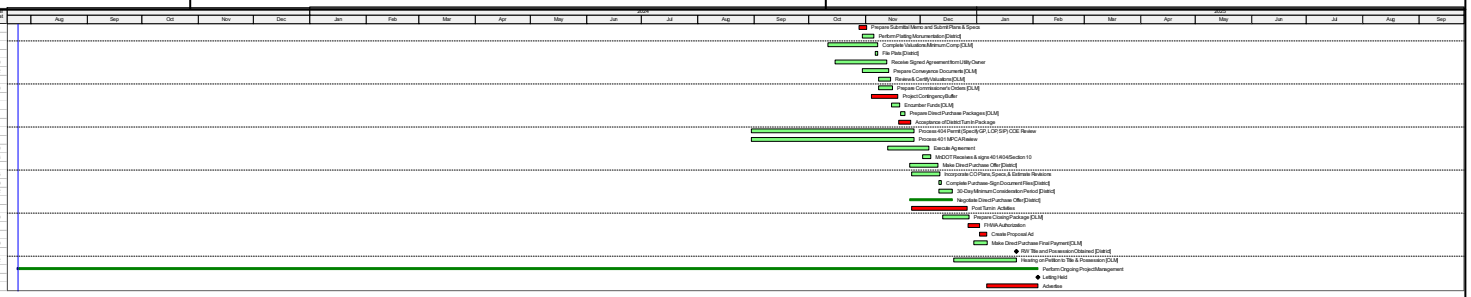

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining ...

TASK filter: All Activities
